BOREWELL
COMPLETION REPORT

VINAYAKA ENTERPRISES

Borewell Drilling Contractors

Mobile : +91 9342202932 / 9343202932

No. 9, Bhadrappa Layout, Bhadrappa Compound, Near Hebbal, Ring Road, Bangalore 560094

No. : 971

Date : 22/Jul/18

1. Customer's Name and Address : Assistant Executive Engineer
   with Telephone No. Vidyaranyapura Sub Division
   BBMP. Banglore-97.
2. Well Location : Ramachandrapura park
3. Total Well Depth / Drilled in Ft. : 995ft
4. Casing Erected in Ft. : 210ft
5. Water Struck at the Depth of : 900ft
6. Total Yield (Measuring method "V" Norch : 2'½" / Inches on "V" Norch)
7. Formation of Soil/Well Water Condition : Boulders/Silt/Loose Soil/Clear 900ft
8. At the Depth of : 900ft
9. Recommended to use Jet Pump / Air Compressor / Submersible /Hand Pump

The Borewell was drilled in accordance with the company terms and conditions and handed over to customer in good/ satisfied / Party agreed conditions.

Once the well handed over to party, company is no way responsible for further developments if anything in the well or what so ever.

Party's Signature

I, owner of the Well / (Authorised signatory) fully understood the terms and conditions and the well completion report, I also fully understood the quality and quantity of water from the well duly depend upon the nature / formation of ground water and the drilling agency no way responsible for further occurrence / Changes in the bore with full satisfaction. I hereby endorse my signature.

For VINAYAKA ENTERPRISES

Party's Signature

~~Manager~~ / Proprietor

COMPLETION REPORT

VINAYAKA ENTERPRISES

Borewell Drilling Contractors

Mobile : +91 9342202932 / 9343202932

No. 9, Bhadrappa Layout, Bhadrappa Compound, Near Hebbal, Ring Road, Bangalore 560094

No. : 970

Date : 22/04/18

1. Customer's Name and Address with Telephone No. : Assistant Executive Engineer
Vidyaranyapura Sub Division
BBMP, Banglore-

2. Well Location : Ganesh Layout

3. Total Well Depth / Drilled in Ft. : 985 FT

4. Casing Erected in Ft. : 200 FT

5. Water Struck at the Depth of : 840 FT

6. Total Yield (Measuring method "V" Norch : 2½ / Inches on "V" Norch)

7. Formation of Soil/Well Water Condition : Boulders/Silt/Loose Soil/Clear

8. At the Depth of : 840 FT

9. Recommended to use Jet Pump / Air Compressor / Submersible /Hand Pump

The Borewell was drilled in accordance with the company terms and conditions and handed over to customer in good/ satisfied / Party agreed conditions.

Once the well handed over to party, company is no way responsible for further developments if anything in the well or what so ever.

Party's Signature

I, owner of the Well / (Authorised signatory) fully understood the terms and conditions and the well completion report, I also fully understood the quality and quantity of water from the well duly depend upon the nature / formation of ground water and the drilling agency no way responsible for further occurrence / Changes in the bore with full satisfaction. I hereby endorse my signature.

For VINAYAKA ENTERPRISES

Party's Signature

Manager / Proprietor

Am An GEO CONSULTANT

NAGARAJ MOKASHI, MSc.,
GEOLOGIST

Mobile : 94483 13401
e-mail : ngmokashi@rediffmail.com
am.an4geoconsultant@gmailcom

Ramjyothi Nagar, R.V.College Post, Bangalore - 560 059.

To,

Date :

GEO-TECHNICAL SURVEY REPORT

(Ground Water Exploration)

Sir / Madam,

As per your work order/request Geo-Hydrological / Geo-physical Survey carried out in your land / site belonging Banglore city/village Ramachandrapura pone Dated on 18/04/18 in order to assess the ground water potential of the area for drinking / irrigation / industrial purposes.

The area inspected has a slope towards E/W marked by Black Soil, uneven topography hydrogeological features are found to be favourable / not favourable for ground water extraction. Geology of the area is marked by Soft rock.

SOURCES EXTRACTED :

(I) Betwen 280ft 410ft ft/mtrs. (II) 650ft 780ft ft/mtfs.

(III) 950ft 1000ft ft/mtrs.

From the study of the above field observation, Investigation results, a borewell VES drilling 850 to app depth of 980ft ft/mtrs. Below the ground level, casing pipe required be to app depth of 210ft ft/mtrs.

Approx, yield expected may be around 3800 GPH.

Suggested to drill 4 1/2" / 6 1/2" dia Borewell.

****

NOTE : Although the best site for drilling has been suggested, no guarantee of success can be given and we will not be liable in any way for any loss to the party in respect of the well drilled at the site recommended being a failure in any form.

Nagr

(NAGARAJ MOKASHI)

Save Water

SAVE ENVIRONMENT ADOPT RAINWATER HARVESTING

Services : Ground Water location by geo-hydrological, geophysical and divining methods, Drilling advisors and supervision. Rain Water harvesting, water shed management, Quarry operations, Planning, Water testing, Soil Testing & Surveying.

Am An GEO CONSULTANT

NAGARAJ MOKASHI, MSc.,
GEOLOGIST

Mobile : 94483 13401
e-mail : ngmokashi@rediffmail.com
am.an4geoconsultant@gmailcom

Ramjyothi Nagar, R.V.College Post, Bangalore - 560 059.

To,

Date :

GEO-TECHNICAL SURVEY REPORT

(Ground Water Exploration)

Sir / Madam,

As per your work order/request Geo-Hydrological / Geo-physical Survey carried out in your land / site belonging Banglore city/village Ganesh Layout Dated on 18/04/2018 in order to assess the ground water potential of the area for drinking / irrigation / industrial purposes.

The area inspected has a slope towards N/W marked by Red Soil, uneven topography hydrogeological features are found to be favourable / not favourable for ground water extraction. Geology of the area is marked by Hard rock.

SOURCES EXTRACTED :

(I) Betwen 350 FT 500FT ft/mtrs. (II) 610FT to 750FT ft/mtrs.

(III) 850 FT 1000FT ft/mtrs.

From the study of the above field observation, Investigation results, a borewell VES drilling 850F to app depth of 950FT ft/mtrs. Below the ground level, casing pipe required be to app depth of 200FT ft/mtrs.

Approx, yield expected may be around 3400 GPH.

Suggested to drill 4 $\frac{1}{2}$" / 6 $\frac{1}{2}$" dia Borewell.

****

NOTE : Although the best site for drilling has been suggested, no guarantee of success can be given and we will not be liable in any way for any loss to the party in respect of the well drilled at the site recommended being a failure in any form.

Save Water

(NAGARAJ MOKASHI)

SAVE ENVIRONMENT ADOPT RAINWATER HARVESTING

Services : Ground Water location by geo-hydrological, geophysical and divining methods, Drilling advisors and supervision. Rain Water harvesting, water shed management, Quarry operations, Planning, Water testing, Soil Testing & Surveying.

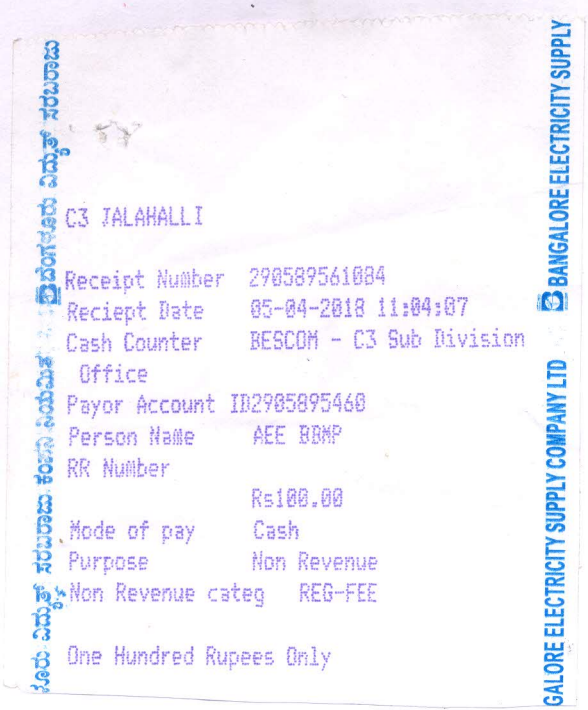

C3 JALAHALLI

Receipt Number 290589561084
Reciept Date 05-04-2018 11:04:07
Cash Counter BESCOM - C3 Sub Division Office
Payor Account ID2905895460
Person Name AEE BBMP
RR Number
Rs100.00
Mode of pay Cash
Purpose Non Revenue
Non Revenue categ REG-FEE

One Hundred Rupees Only

BANGALORE ELECTRICITY SUPPLY COMPANY LTD

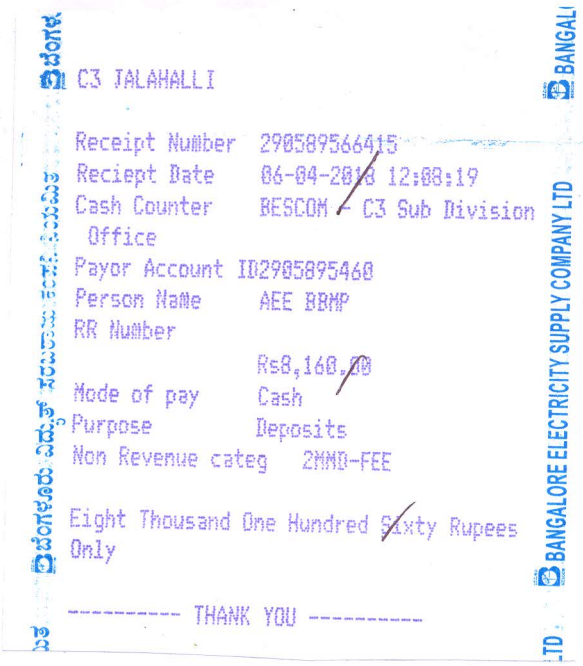

C3 JALAHALLI

Receipt Number 290589566415
Reciept Date 06-04-2018 12:08:19
Cash Counter BESCOM - C3 Sub Division Office
Payor Account ID2905895460
Person Name AEE BBMP
RR Number
Rs8,160.00
Mode of pay Cash
Purpose Deposits
Non Revenue categ 2MMD-FEE

Eight Thousand One Hundred Sixty Rupees Only

---------- THANK YOU ----------

BANGALORE ELECTRICITY SUPPLY COMPANY LTD

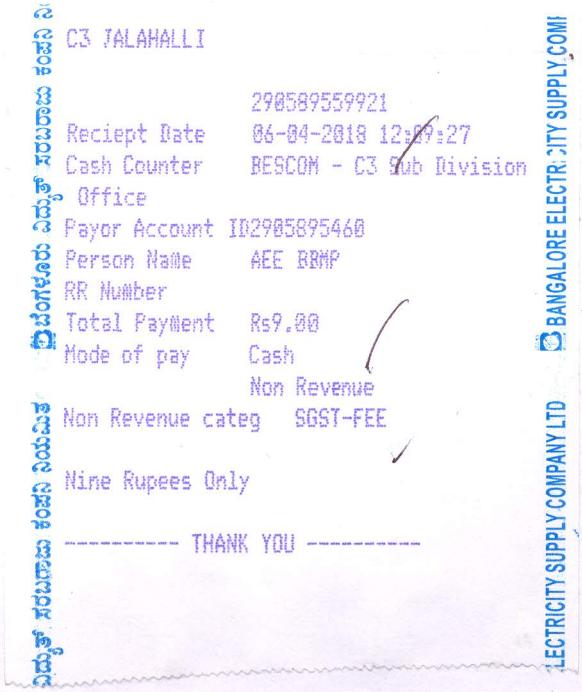

C3 JALAHALLI

290589559921
Reciept Date 06-04-2018 12:09:27
Cash Counter BESCOM - C3 Sub Division Office
Payor Account ID2905895460
Person Name AEE BBMP
RR Number
Total Payment Rs9.00
Mode of pay Cash
Non Revenue
Non Revenue categ SGST-FEE

Nine Rupees Only

---------- THANK YOU ----------

BANGALORE ELECTRICITY SUPPLY COMPANY LTD

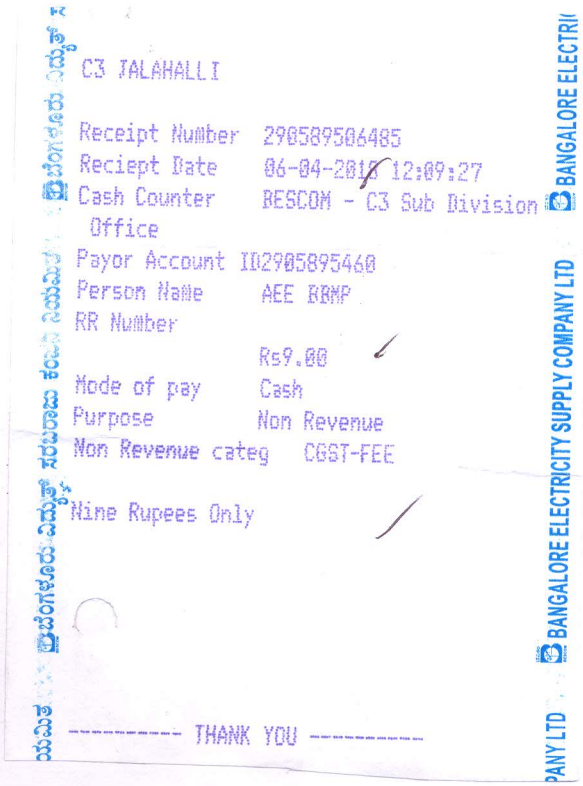

C3 JALAHALLI

Receipt Number 290589506485
Reciept Date 06-04-2018 12:09:27
Cash Counter BESCOM - C3 Sub Division Office
Payor Account ID2905895460
Person Name AEE BBMP
RR Number
Rs9.00
Mode of pay Cash
Purpose Non Revenue
Non Revenue categ CGST-FEE

Nine Rupees Only

---------- THANK YOU ----------

BANGALORE ELECTRICITY SUPPLY COMPANY LTD

TAX INVOICE

(See Rule 46 of the Central Goods & Services Tax Rules, 2017)

Landis+Gyr Limited

ಲ್ಯಾಂಡಿಸ್+ಗೇರ್ ಲಿಮಿಟೆಡ್

Landis+Gyr

R. O. Address :
No. 503, 1st Floor, 3rd Main,
50 Feet Road, Hanumanthnagar,
BENGALURU - 560050.
Ph.: 080-26678515

Branch Office Address :
O/o AEE (C, O&M), C-7 Sub-Divison,
BESCOM, Yelahanka,
BENGALURU - 560064.

Customer Name AEE BBMP

Address W.No-11
R.C.pura.
B.L

GSTIN :

BILL No. **YNK/18/** 00260 ~~013260~~

DATE : 10/04/18 TIME : 4.45 AM/PM

GSTIN : 29AAACV9922B1ZA

Sl. No.	Description of Goods / Services	Quantity (Nos.)	Rate per Pc Rs.	Value Amount Rs.	P.
	HSN Code : 90283010 Single / Three Phase Static Energy Meter Model : E150 / E250, 5-30 Amps Serial Nos.				
	3ph CS C7555596	01	1466.67	1466.	67

BESCOM DVN : C.J

W.O. No. G. 12083 Date 09/04/18

Total Invoice Value (In Words) : One Thousand four hund Thirty Sixty four paise

CGST @ 9%	132.	4
SGST @ 9%	132.	00
GRAND TOTAL	1730.	67

E.&O.E.

1st Copy Original : White
2nd Copy Duplicate : Pink
3rd Copy Triplicate : Yellow
4th Copy Extra : Blue

For **Landis+Gyr Limited**

Signature
